

East Side Interceptor Lining Project

Conveyance System Improvements in Renton

Eastside Interceptor Lining Project - update for the week of June 14-20

The [Eastside Interceptor \(ESI\)](#) is one of the main sewer lines that brings wastewater from eastside homes and business to the South Treatment Plant in Renton. This project will repair about 3,700 feet of the line, which is corroded and nearing the end of its service life (see [map](#) below).

For June 14-20, the contractor is finalizing preparations for pipe lining work that will begin soon:

- **Project staging area:** The contractor is finishing their set-up for the project at the Boeing work site, including hooking up the bypass pumps and lines.
- **Minimal night work on Logan Avenue:** The bypass pipe is in place and lining work will not begin until the pipe has been tested. There is no work planned in the street and any night work and traffic control would be for unanticipated work, such as pipe adjustments or repairs.
- **Barriers along Logan Avenue:** Barriers have been set up around the bypass pipes to protect them. This is an active construction area – do not touch or cross the barriers or walk alongside them, or through the work area. Please cross the street to find safe areas to walk.
- **The bike lane** alone Logan between Park Avenue and N 6th Street is closed due to construction. Please cross over to the east side of Logan Avenue or take an alternate route.

Bypass pipe installation is now done. The contractor plans on testing the bypass this Friday and Saturday to make sure it is working correctly.

- Following successful testing of the bypass, flows will be diverted from the ESI into the bypass pipe. **Work inside the ESI pipe will then begin and pumps in the staging area will begin operating around the clock.** Noise monitoring measures are in place.
- Once in-pipe work begins, there will be **temporary daytime lane closures on Logan Avenue** so crews can access the pipe.


Burnett Avenue will remain closed at N 6th Street for several months. For this week, only a few days of work are planned for this area. Work could be days or nights.

Please see the [website for more details](#) and to sign up for construction updates.

For more information

Visit the [project website](#) to learn more about the project and to sign up or manage project updates.

For more information, contact David Freed at 206-263-9453 or david.freed@kingcounty.gov.

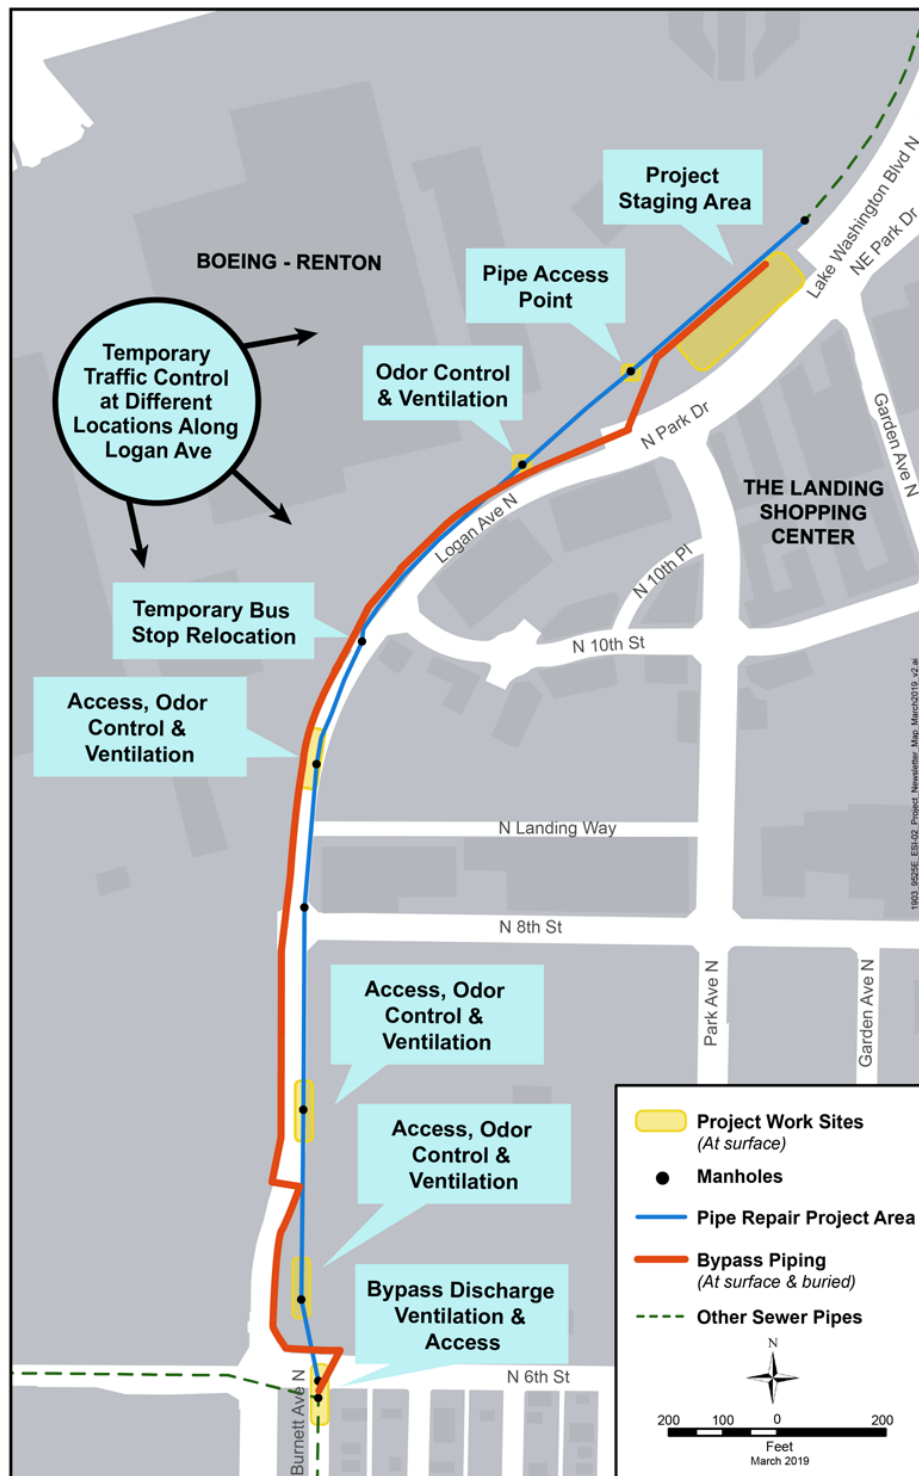

Project area

Alternative Formats Available - 206-477-5371 - TTY Relay: 711
